




JUL 11 2005



## Special Project to Support the Reintegration of Ex-combatants in the Framework of the Peace Process in Angola

### Quarterly Report April - June 2004



#### Table of contents:

I. INTRODUCTION.....	2
II. ACTIVITIES IMPLEMENTED .....	2
1. SUPPORT TO IRSEM.....	3
2. AGRICULTURAL REINTEGRATION .....	7
3. ECONOMIC REINTEGRATION .....	10
III. CONSTRAINTS & DIFFICULTIES .....	13
IV. FINANCIAL SUMMARY.....	14
V. PRIORITIES FOR THE III QUARTER OF 2004. ....	15
ANNEXES .....	16

## Overall Objective of the Special Project

---

*To contribute to the demobilization and reintegration program of the Government of Angola for the promotion of national security, peace and development through the economic and social reintegration of ex-combatants and their families into civil society.*

## Summary of Special Project's Activities during the II Quarter 2004

---

### **Component 1: Capacity built to plan and manage the future ADRP programme**

- ✓ Training of 96 technicians and managers from IRSEM in the ADRP Implementation Manual.
- ✓ Dissemination of the ADRP Implementation Manual.
- ✓ Design of a proposal to develop the MIS of the ADRP.

### **Component 2: Ex-combatants reintegrated into the agricultural production**

- ✓ Continuation of the distribution of the agricultural kits.
- ✓ Design of the database to register the beneficiaries of the seeds and tools distribution. As of June 28, 10.060 out of 50.000 were recorded in the database.
- ✓ Preparation of the training materials and start up of the training of NGO's field monitor.

### **Component 3: Economic reintegration activities**

- ✓ Procurement and adjudication of the tool kits.
- ✓ Launching of the Business Training, Business Advisory Services and Micro Credit programs.
- ✓ Monitoring of the implementation of the subprojects.

## Main Priorities for the Upcoming Quarter

---

- Conclusion of the distribution of the seeds and tools.
- Distribution of the tool kits to the selected beneficiaries.
- Monitoring of the implementation of the Business Training, Business Advisory Services and Micro Credit programs.
- Finalization of the independent audit and independent evaluation of the Project.



Angola

## I. INTRODUCTION

This is the third quarterly report on the implementation of the Special Project to support the reintegration of ex-combatants in the framework of the peace process in Angola.

During the period of April to June 2004, besides the activities planned under the components of the Project - agriculture reintegration, economic reintegration and support to IRSEM – the project supported the launching of the ADRP in Huambo (Calenga Community) on the 27 April 2004, following the approval of the program on March 2, 2004 and the approval of the Implementation Manual.

The implementation of a program like the ADRP involves an enormous amount of planning and effort. Due to the scarcity of qualified human resources, this process has necessitated the full involvement of the Special Project consultants. In this context, many of the activities implemented during the past Quarter were concentrated in the dissemination of the ADRP implementation manual and the creation of the basic conditions for an efficient implementation of the reintegration program.

As with the previous reports, the current report includes the consolidated financial information and the status of the procurement of goods and services for the period of April to June 2004. It also includes a summary of the activities implemented under the CIDA Project<sup>1</sup>, which is a complement of the current project.

## II. ACTIVITIES IMPLEMENTED

Based on the priorities defined for the Quarter, namely:

- (i) Conclusion of the distribution of the agricultural kits;
- (ii) Receipt and consolidation of Implementing Partners reports;
- (iii) Preparation of a database to register the beneficiaries by province and municipality;
- (iv) Training of NGO's field monitor on specific market gardening methodologies;
- (v) Evaluation of the coverage of the agricultural input distribution and determination of the need for a follow-up distribution to remaining ex-combatants;
- (vi) Monitoring the implementation of the economic reintegration subprojects.

---

<sup>1</sup> / Annex 1

The activities implemented by component are summarized below:

## 1. Support to IRSEM

### (i) Training of IRSEM staff at Central and Provincial Level, the Implementing Partners and the Local Authorities

The objective of the activities implemented was to (a) train the staff in the use of the Implementation Manual to allow them to participate actively and efficiently in the implementation of the ADRP and (b) disseminate the manual to the institutional and implementing partners of the reintegration program.

In this context the following activities were implemented:

- a. Elaboration of the training materials;
- b. Training of 16 technicians from IRSEM Central in a seminar held from April 13-15, 2004;
- c. Training of 20 technicians from IRSEM Benguela, Huambo, Bié and Kwanza Sul, in a seminar held in Huambo;
- d. Between May 4-6, 2004, three seminars were held in Luanda, Malange and Lubango to train 60 technicians from the remaining provincial delegations of IRSEM, as indicated in the table below:

Local	Provincial Delegations of IRSEM
Luanda	Luanda, Bengo, Zaire and Uíge
Malange	Kwanza Norte, Malange, Lunda Norte, Lunda Sul and Moxico
Lubango	Cunene, Kuando Kubango, Huíla, Cabinda and Namibe

Participants were subject to an evaluation test at the beginning and the end of each seminar.

In the five seminars, the Special Project team trained a total of 96 technicians and managers from IRSEM.

### (ii) Dissemination of the Implementation Manual

The consultants of the project continued the support to the dissemination of the Implementation Manual. According the plan defined by IRSEM, 10 seminars were conducted in the following provinces: Huíla, Malange, Huambo, Benguela, Kuanza Sul, Bié, Kuando Kubango, Lunda Norte, Lunda Sul and Moxico. The seminars were primarily directed to the provinces with the highest concentration of ex-combatants.



Angola

This activity will be continued in the next Quarter to cover the remaining provinces.

**(iii) Definition of the Terms of Reference to Contract the Strategic Partners**

Support was provided to the definition of the Terms of Reference for the agencies – Strategic Partners – that will provide technical assistance to IRSEM for the implementation of the ADRP. The proposed terms of reference were approved by IRSEM and submitted for the approval of the World Bank.

**(iv) Support to the design of the Terms of Reference for the participation of the Implementing Partners in the ADRP**

The seminars conducted in the provinces as indicated above had a strong practical component in order to prepare the provincial delegations of IRSEM for the implementation of the immediate activities under the ADRP. Participants of the seminars have identified the following priority tasks to be implemented:

- Establishment, in coordination with the provincial Governments, of the provincial committees for the evaluation of the subprojects;
- Definition of the regulations for the provincial committees;
- Definition of the Terms of Reference to contract the Implementing Partners; and
- Selection of implementing partners with recognized capacity.

The establishment of the provincial committees and the design of the Terms of Reference to contract the implementing partners are the two main important tasks that have to be developed to initiate the implementation of reintegration activities in the framework of the ADRP.

As the activities under the ADRP are demand-driven, is essential that the design of the Terms of Reference be based either on existing local reintegration studies, or on those to be undertaken in the main municipalities where the ex-combatants are located.

In this context, the Special Project, with the support of the national consultant hired for Benguela, has supported the following activities:

- Update of the local reintegration studies of Balombo, Bocoio, Ganda, Cubal and Chongoroi, the five municipalities of Benguela Province with the highest concentration of ex-combatants;
- On the basis of these studies, the consultant prepared the Terms of Reference to recruit the implementing partners. The Terms of Reference

were approved by IRSEM and later published at the provincial level. These implementing partners will assist around 4,000 ex-combatants.


(v) **Design of the Questionnaire to Update the Data on the ex-combatants.**

Considering that the statistical information on the ex-combatants is from 2002 (collected in the gathering areas during the demobilization process), it was considered important to update this information. In this context a survey is being prepared (for selected municipalities) and will be jointly financed by the Special Project and the ADRP.

The objective of this survey is to:

- Improve the information of the target group;
- Furnish to the implementing partners updated and accurate information regarding the beneficiaries of the programs they will serve;
- Establish a baseline that will support the monitoring and the impact evaluation of the projects.

The figure below illustrates the preparation, execution and monitoring process of the implementing partners' proposals:

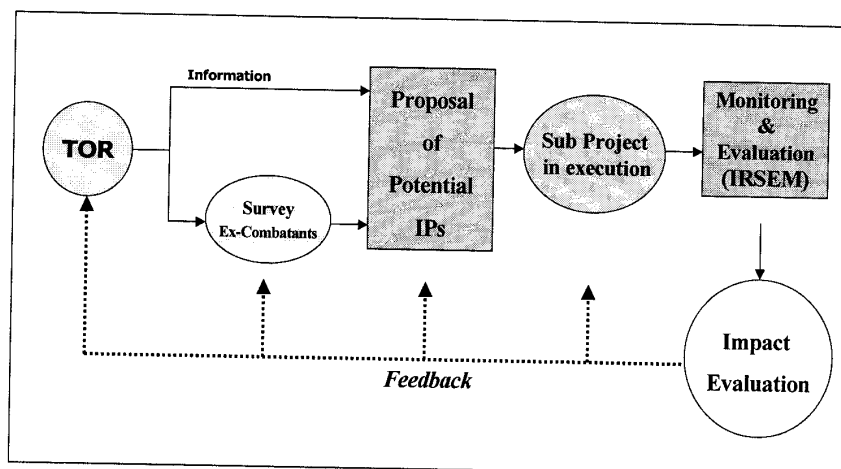

The proposed questionnaire is included in Annex 2.

(vi) **Management Information System**

Based on the request from IRSEM to support the design of the Management Information System (MIS), a consultant was hired by the Special Project to develop the following activities:

- Perform a detailed diagnosis of IRSEM informatics' system and proposed recommendations for its improvement including the alternatives for the design of the MIS;
- Design of 4 databases to monitor the program benefits – contingency subsidies; reinstallation kits, agriculture kits (already used by FAO) and food ration. These databases will later be integrated in the MIS;
- Conversion of the previous databases (Bicesse and Lusaka) to a format that will be compatible with the future MIS;
- Design of a proposal to develop the MIS of the ADRP;
- Participate in the selection of the national consultants that will work with the system and definition of his tasks;
- Discuss with the Financial Management and Procurement Unit (FMPU) and potential suppliers of satellite communications systems.

The proposal of the MIS for the ADRP (see Annex 3) was approved by IRSEM and is being developed by the consultant. The proposed system will link IRSEM at the Central level with the provinces and will provide timely information for the monitoring of the subprojects and planning and design of specific activities to support the effective reintegration of the ex-combatants.

The MIS will include information regarding (i) the interviews of the ex-combatants; (ii) proposals for implementation of the services to be provided to the ex-combatants; (iii) control of the implementing partners contracts; (iv) benefits provided; (v) control of the resources and (vi) monitoring and evaluation.

#### **(vii) Other activities to support IRSEM Management**

The consultants of the Special Project provided continuous support to the senior management of IRSEM as well as to the different departments directly involved in the implementation of the ADRP. The following activities should be highlighted:

- Definition of the Terms of Reference to hire the regional/provincial advisors and the senior M&E specialist;
- Proposal of the contract agreement for the municipal liaison officers (*assistentes rurais*). The first group of 16 municipal liaison officers will begin working this July 2004;
- Senior management support of IRSEM in the negotiation of the European Union's (13.5 million Euros) contribution to the ADRP;
- Support to the creation of the central and provincial commissions for the project proposals approval. It is expected that the commission to be established at the central level will be effective from July 2004.



Angola

## 2. Agricultural Reintegration

### (i) Continuation of the distribution of the agricultural kits

The methodology set up with IRSEM for the distribution of kits allows for the maintenance of strategic stocks at the provincial level in order to cover 1) unexpected caseload in the priority municipalities and 2) non priority municipalities. In the majority of the cases, the actual number of beneficiaries by province was lower than initially expected. The distribution of the remaining kits by province was as follow (detailed figures are presented in Annex 4):

Huambo: The NGO OIKOS covered the remaining municipalities. 1.000 kits were sent from the Huambo provincial stock to the North of Huila to be distributed in Chipindo where the caseload was higher than expected.

Huila: The remaining kits were distributed in municipalities uncovered during the 1<sup>st</sup> phase of distribution. The implementing partners (IPs) and IRSEM requested additional kits from Huambo and Lobito to ensure full coverage of the caseload of the province.

Bié: The NGO CARE reported that only 78% of the kits were distributed in the project area. This means that at the time of distribution there were fewer beneficiaries than expected, but according to IRSEM, movements of ex-combatants were registered in the southern part of the province. This may increase the total number of demobilized soldiers in the province. Instructions were given to the NGO to conclude as soon as possible the distributions.

Kuanza Sul: The remaining kits are being distributed by the NGO Save the Children US. The process was delayed due to the fact that IRSEM wanted to choose additional municipalities although all the kits were not yet distributed in each municipalities. The mobilization of IRSEM staff is also a constraint for the distributions in the municipality of Mussende, where distribution of the kits in São Lucas will only be completed the first week of July, 2004, when an IRSEM official will go to this Municipality.

Benguela: The remaining kits were distributed by the NGO Horizonte in Ganda municipality, where several demobilized soldiers were registered during the first phase of the distribution.

Specific case of Kuando Kubango: The distribution in Kuando Kubango province was not initially planned. It was initially estimated that there were 50.000 ex-combatants in the 5 provinces of the Planalto. In fact, in each of these provinces, there were fewer ex-combatants than estimated,





Angola

therefore creating excess stocks, which were available for distribution in Kuando Kubango.

According to IRSEM data, 9.700 ex-combatants are living in the municipality of Menongue. In coordination with IRSEM, it was decided that the remaining 8.000 kits would be sent from the Lobito warehouse to Menongue. The NGO Caritas was contracted for the distribution. The implementing partner encountered the same difficulties as already mentioned for the distribution in the other 5 provinces, namely:

- Lack of beneficiary registry;
- Lack of comprehension from the local IRSEM office which insisted to include in the distribution small groups of beneficiaries living in the cities on the border line with Namibia. The number of potential beneficiaries was not sufficiently large to justify logistical costs for the transport of the kits from Menongue to the southern border.

These problems were solved and the distribution is on-going; IRSEM is slowly releasing the different beneficiary lists. It also appears that the estimated number of beneficiaries was higher than reality. This may be due to the fact that the demobilized soldiers moved from Kuando Kubango, where they were not receiving the kind of support available in other provinces (Bié and Huila).

#### **(ii) IRSEM database**

The lack of a specific beneficiary registry was the major constraint for the implementation of the activities under this project. The implementing partners had to rebuild beneficiaries' lists during the distribution phase; this considerably delays the distributions.

It was agreed with IRSEM that FAO would build a simple database based on these distributions. IRSEM received the support of a specialist, who created a complete database for the demobilization process.

This database was given to FAO, which recruited a national consultant on a part time basis to record the distribution data into the new database.

The database for distribution is user friendly; the key used is the NIP of each demobilized soldier. Information regarding the date, place (Province/ municipality/ commune/ local of distribution), and Implementing Partner are registered in the database. As of June 28, 2004, 10.060 out of the 50.000 data were already recorded in the database.



Angola

Some NGOs noted that an IRSEM official was not always present during the distributions or had delegated an official from MINARS to follow the distributions.

**(iii) Training of NGO's field monitor on specific market gardening methodologies**

The training and the support to the ex-combatants who received the agricultural kits is a key component of FAO support under the Special Project. The implementation of this activity was delayed due to several technical problems with the printing of the training materials.

In early June, FAO recruited an additional national consultant in order to reinforce the training capacity of the FAO team. With the support of this consultant, the training materials were reviewed and improved and a training curriculum was designed, taking into account the specificity of the beneficiary group and the timeframe of the training activities.

– Training curriculum

The training is designed for trainers, with basic technical skills in agriculture. The trainees will be part of NGO staff, IDA and EDA staff at provincial level and interested staff from IRSEM. The following basic themes will be developed during the training:

- Cereals: production and conservation of seeds;
- Pulses: production and conservation of seeds;
- Vegetable: importance in the diet, production techniques;
- Organic fertilizers: how to prepare, how to use.

– Training Materials

The trainees will receive:

- 3 modules documentation (with coloured pictures)
- Kits of posters for posting and training the community.

– Training schedule

The training activities will be implemented on the dates indicated below:

Province	Place	Timeframe	Expected participation	NGOs
K. Sul	Sumbe	28 & 29/06	22	Solidarités, ASBC, SCF-US,
Benguela	Benguela	1 & 2/07	22	Horizonte, Okutiuka, AAA
Huambo	Huambo	5 & 6/07	22	Wvi, AASAA, Oikos, Movimundo
Huíla	Huíla	13 & 14/07	22	ACF, Zoa, Oikos, CNR, ALISEI
K. Kubango	Menongue	20 & 21/07	22	Caritas
Bié	Kuito	29 & 30/07	22	CARE, Movimundo,

### 3. Economic Reintegration

#### (i) Complementary Resources to the Special Project

A complementary project was negotiated with the Spain Cooperation (see summary in Annex 5). The project in the amount of 100.000 Euros will support the rehabilitation of five Schools of Arts and Crafts in Benguela (2), Huíla, Huambo, and Malange provinces that will benefit around 250 ex-combatants. In the framework of this project, a subproject was designed for the province of Benguela – Ganda Municipality – *Missão Católica do Ndunde*. The contract for the implementation of this subproject was recently signed and the Special Project and the Spain Cooperation project will jointly finance it.

#### (ii) Economic Reintegration Subprojects


An important part of the Special Project staff time was dedicated to the monitoring of the subprojects being implemented in the five provinces. On the basis of the progress reports presented by the subprojects, the payment of the second instalment was made for some subprojects in the different provinces (see Annex 6).

During this Quarter a contract to finance vocational training and community works in Benguela – *Missão Católica do Ndunde* – was signed and the actual situation of the reintegration subprojects is as follows:

Project	Amount (US\$)
CIDA	154.691
Special	1.056.266
<b>Total</b>	<b>1.210.957</b>

The distribution of the resources from the Special Project for the implementation of the pilot subprojects is as follows:

Component	Amount (US\$)
Vocational Training	596.955
Business Training	19.580
MBD Services	10.400
Micro Credit	60.000
Community Works	198.891
<b>Sub-Total</b>	<b>885.826</b>
Tool Kits/Economic Reinteg.	170.440
<b>Total</b>	<b>1.056.266</b>

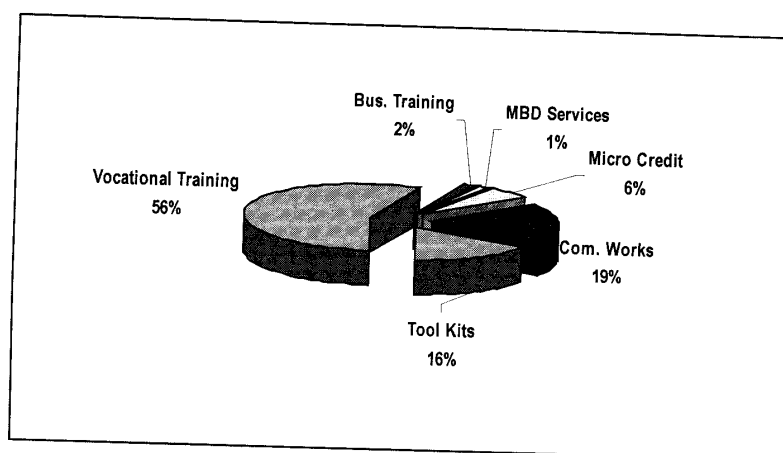

The distribution of the Subprojects by Province is as indicated below:


Province	Nr Prop.	Amount (CIDA & SP)	Beneficiaries
Benguela	4	131.223	592
Bié	8	78.190	312
Huambo	9	171.951	1.016
Huíla	9	406.978	1.598
Kwanza Sul	14	252.175	1.387
<b>Total</b>	<b>44</b>	<b>1.040.517</b>	<b>4.905</b>

### (iii) Business Training, Business Advisory Services and Micro Credit

Under this component of the project, the following activities were implemented:

- Definition of Terms of Reference for the recruitment of the implementing partners for both the MBA Services and Micro Credit;

- Identification of the beneficiaries that will be involved in the pilot experiment. Approximately 1.000 beneficiaries – women ex-combatants and widows from ex-combatants – were identified in Huambo (capital and municipality of Caala) to participate in the pilot projects of Micro-business training, advisory services and micro credit;
- Selection of the implementing partners with recognized capacity, e.g. INAPEM<sup>2</sup>, Development Workshop (DW) and *Centro Maite Marcelino*;
- Clarification of the steps and procedures for the implementation of the programs. The figure below illustrates the implementation process of these components.

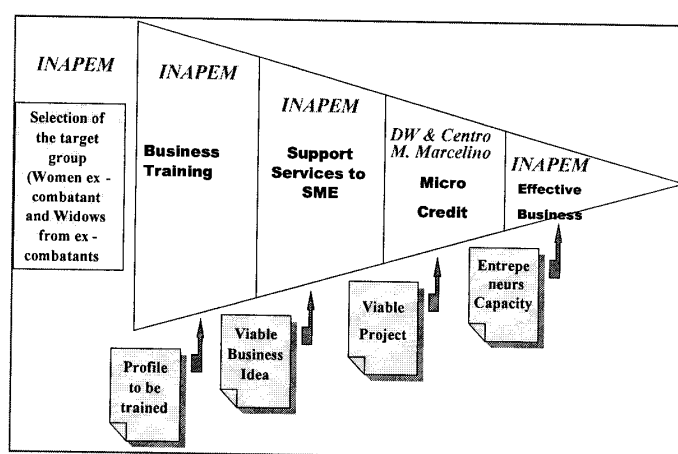

The training will be provided by INAPEM. From this group and on the basis of a test of entrepreneurship ability aptitude, a smaller group will be selected to benefit from the 80 hour (min) business training.

The beneficiaries who present a valid business idea will receive support from INAPEM for the preparation of a business project that will then be submitted to a DW and *Centro Maite Marcelino*.

For the implementation of the Micro Credit component, the agreements are being discussed with the above indicated implementing partners. It is foreseen that the credit will benefit 100 women in the first phase. On the basis of the reimbursement of this amount, a second group of 100 women will benefit. It is expected that a total of 400 women will benefit from this program (200 by each institution).

The amount of the credit to be provided is of US\$ 300 for those who:

- Have received basic business training provided by INAPEM;
- Have submitted a valid business proposal;
- Have capacity to reimburse the loan in the time defined.

<sup>2</sup> / INAPEM - Instituto Nacional de Apoio a Pequenas e Médias Empresas

**(iv) Tool Kits**

After launching the tender for the acquisition of the tool kits in March 2004 and as a result of the weak participation (2 out of 7 enterprises have submitted the bids), the project, after meeting the participating enterprises, re-launched the tender and redefined the evaluation criteria.

The proposals were evaluated in two stages:

- In the first stage the proposals were evaluated using the criteria price (70%) and delivery time (30%).
- The first classified enterprises were then asked to provide samples of the tool kits in 20 days (corresponding to 60% of the value of each lot).

The samples were evaluated by the evaluation committee, integrating the reintegration expert, the UNDP procurement officer and three professional trainers hired for this purpose.

A total of 625 tool kits are being purchased, with a total amount of US\$ 170.439,98 (corresponding to a unit cost of US\$ 272,70).

The information on the adjudication of the tool kits is included in Annex 7.

### **III. CONSTRAINTS & DIFFICULTIES**

The main difficulties and lessons learned can be summarized as follows:

- The Special Project consultants were asked to perform many other tasks in support of the preparation of the implementation of the ADRP. The need to implement the ADRP in accordance with the agreements signed and the procedures defined in the implementation manual will require additional support to IRSEM, in particular at provincial level. Many of the activities planned and initiated with the support of the technical assistance are not continuing due to weak capacity of the personnel in the provinces.
- The delay in the recruitment of the strategic partners may negatively affect the needed support to the 140.000 beneficiaries the ADRP has to support in the next 3 years.
- Besides the efforts undertaken by the Special Project to train IRSEM staff at the provincial level, capacity building at the provincial level should continue to be a priority. The possibility to support some of the provincial delegations of IRSEM with continued technical support by posting national advisors, should be evaluated;




Angola

- The main difficulties in the distribution of the agricultural kits is related with the registry of the beneficiaries;
- Due the difficulties related with the acquisition of the tool kits for the economic reintegration component, it is important to evaluate the possibility of an international competitive bidding process. In this context, there is a need to plan in advance the procurement of these goods;
- Regarding the implementation of the subprojects, the main problems are related with the capacity of the implementing partners to report on the implementation. This has required additional effort from the Special Project team to support the implementing partners. The selection of more capable organizations may improve the reporting and the execution speed of those subprojects.

#### IV. FINANCIAL SUMMARY

During the current quarter a total of US\$ 528.594 was spent in the implementation of the project activities.

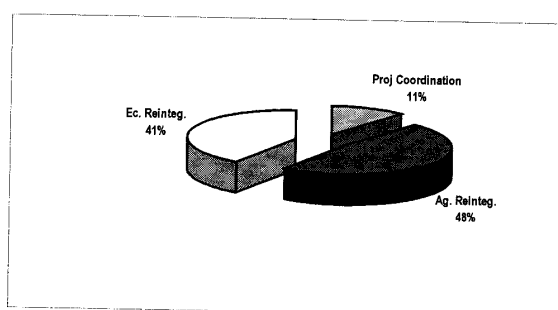

By component the distribution of the amount spent during the quarter is as illustrated in the figure.

The majority of the resources spent were on the implementation of the activities under the Agriculture Reintegration. It should be

underlined that 47% of the resources spent under this component was for the payment of the distribution costs of the seeds and tools (contracts with NGOs, at 3USD per kit distributed).

By category the distribution of the amount spent is as indicated in the following table:

Category	US\$
Goods	0
Training, Seminars, Wksp	150.267
Consultants & Audits	147.894
Micro-Grants	0
Employment Support	56.855
Operating Costs	173.577
<b>Total</b>	<b>528.594</b>



Angola

The operating costs include the costs of the distribution of the seeds and tools to the beneficiaries (payments to the NGOs above mentioned).

The total amount spent from September 2003 to June 2004 represents 60% of the total budget approved for the Special Project.

Category	Sep-Dec 03	Jan-Mar 04	Apr-Jun 04	TOTAL
Goods	1.555.256	0	0	1.555.256
Training, Seminars, Wksp	0	157.923	150.267	308.190
Consultants & Audits	65.129	76.922	147.894	289.946
Micro-Grants	0	0	0	0
Employment Support	0	45.566	56.855	102.421
Operating Costs	81.068	82.232	173.577	336.877
Unallocated	0	0	0	0
<b>Total</b>	<b>1.701.453</b>	<b>362.643</b>	<b>528.594</b>	<b>2.592.690</b>

#### V. PRIORITIES FOR THE III QUARTER OF 2004.

The following are the main activities planned for the III Quarter of 2004:

1. Conclusion of the distribution of the agricultural kits.
2. Reception and consolidation of the remaining reports from the Implementing Partners of the Agricultural Reintegration Component.
3. Conclusion of the recording data of the beneficiaries of the seeds and tools.
4. Training of the implementing partners
5. Monitoring of the implementation of the subprojects.
6. Conclusion of the subprojects and elaboration of the final reports.
7. Receipt of the tool kits and distribution to the eligible beneficiaries.
8. Technical support to IRSEM in the implementation of the ADRP.
9. External audit and evaluation of the Project.



## Annexes

1. Report CIDA Project
2. Questionnaire to Update the data on the ex-combatants
3. Management Information System
4. Distribution of the Seeds and Tools
5. Summary of the Spain Contribution to the Special Project
6. List of Subprojects
7. Information on the Tender of the Tool Kits
8. Procurement Monitoring Report
9. Sources and Uses of Funds
10. Physical Progress Report

---

## ANNEXES

---

## ANNEX 1 - CIDA PROJECT - BALANCE JUNE 2004

Outputs	Activities Planned for 2004	Responsible Partner	Total Budget (Revised)	Activities Implemented Jan-Jun 2004	Amount Spent June 2004	Balance
Strengthening of capacity of IRSEM to implement vocational training programmes for demobilized ex-soldiers.	ACT1: Strengthen Staff Capacity at provincial level	IRSEM	2,057.99	On the job training provided to IRSEM staff in K.Sul, Huambo, Benguela & Huila	2,057.99	0.00
	ACT2: Improve Working conditions	IRSEM	23,257.92	Purchase of office equipment, ballistic blanket & satellite phone	23,257.92	0.00
		IRSEM	4,407.00	Maintenance costs of the project vehicle	4,126.50	280.50
Economic reintegration activities planned and implemented in 3 selected Municipalities in target Provinces.	ACT3: Design of Local Reintegration Plans & Subprojects	IRSEM	9,272.07	Design of the following reintegration plans: Chongoroi (Benguela), Chinguar, Catabola, N'Harea, Chitumbo (Bié); Chipindo, Kuvango (Huila)	9,272.07	0.00
	ACT4: Implementation of Subprojects	IRSEM, NGOs & Local Adm	42,067.50	Payments of 1st and 2nd installment Benguela Subproject, and 2nd installment Huambo, Benguela and K. Sul Subprojects	30,887.50	11,180.00
	ACT5: Monitoring of the Subprojects	IRSEM	22,672.52	Monitoring of the Subprojects in Huambo, K. Sul and Bié	22,672.52	0.00
Project Evaluation	ACT6: External Evaluation of the Project	IRSEM	15,000.00	Independent Evaluation planned to July 2004	0.00	15,000.00
		IRSEM	1,500.00	Independent Evaluation planned to July 2004	0.00	1,500.00
	Total		120,235.00		92,274.50	27,960.50

## ANNEX 2 – Questionnaire to Update the data on the ex-combatants

**Inquérito aos Ex-Militares**      **Provincia:**      **Município:**      **Comuna:**      **Data:**

**NIP / NCP**

□ □ □ □ □ □ □ □

**Nota prévia:** A entrevista deverá ser conduzida sem pressionar o entrevistado para que as respostas surjam naturalmente e correspondam à realidade vivida pelo beneficiário. Sempre que não se obtiver uma resposta a um determinado item, dever-se-á assinalar que não foi obtida resposta e não "inventar" uma qualquer resposta. É preciso notar que a veracidade das entrevistas será confirmada e reconfirmada através de questionários já antes respondidos pelo Ex-Militar e por novas entrevistas.

### A. Informação geral

Esta informação, embora já existente nos bancos de dados, deverá ser reconfirmada para cada Ex-Militar. Ela destina-se a manter actualizado o contacto com o beneficiário para efeitos de avaliação do impacto, através de futuras visitas.

1. Nome do beneficiário (tal como consta da cédula de licenciamento):	
2. Local de Nascimento (Comuna e Localidade) :	
3. Nome da Mãe:	
4. Morada actual:	
5. Município e Comuna:	

### B. Contexto social

6. Vive com a sua família?	Sim <input type="checkbox"/>	Não <input type="checkbox"/>	Nº de membros ____
7. A comunidade em que se integrou corresponde àquela onde se pretendia instalar aquando da desmobilização?	Sim <input type="checkbox"/>	Não <input type="checkbox"/>	
8. Em caso negativo, qual a(s) razão(ões) para a mudança?			
9. Na comunidade em que se integrou foi bem aceite?	Sim <input type="checkbox"/>	Não <input type="checkbox"/>	
10. Apresente qualquer problema que tenha ocorrido a respeito da sua integração na comunidade / família?			
11. Na comunidade em que se integrou ou na sua proximidade, existe:	Escola? <input type="checkbox"/>	Posto de Saúde? <input type="checkbox"/>	Igreja? <input type="checkbox"/>
12. Tem filhos? Quantos?	Sim <input type="checkbox"/>	Não <input type="checkbox"/>	N.º: ____
13. Os seus filhos vão à escola?	Sim <input type="checkbox"/>	Não <input type="checkbox"/>	N.º: ____
14. Tem Bilhete de Identidade de Cidadão Nacional?	Sim <input type="checkbox"/>	Não <input type="checkbox"/>	N.º: ____
15. E os seus familiares também têm B.I. ou Cédula?	Sim <input type="checkbox"/>	Não <input type="checkbox"/>	Quantos têm? ____
16. Actualmente considera-se plenamente integrado na comunidade?	Sim <input type="checkbox"/>	Não <input type="checkbox"/>	
17. O que poderia ter melhorado a sua integração?			

### C. Contexto económico

18. Qual é a sua situação face ao emprego?	Empregado <input type="checkbox"/>	Conta própria <input type="checkbox"/>	Desempregado <input type="checkbox"/>
19. Tem lavra (terra)?	Sim <input type="checkbox"/>	Não <input type="checkbox"/>	N.º: ____
20. Caso possua lavra, como a obteve?	Família <input type="checkbox"/>	Comunidade <input type="checkbox"/>	Ocupação <input type="checkbox"/>
21. Caso esteja empregado ou a trabalhar por conta própria, tal corresponde ao que pretendia quando foi desmobilizado?	Sim <input type="checkbox"/>	Não <input type="checkbox"/>	
22. O rendimento mensal de sua família, relativamente a um vencimento de 3,000 Kwanzas, é:	Maior <input type="checkbox"/>	Igual <input type="checkbox"/>	Menor <input type="checkbox"/>
23. Caso se encontre desempregado, fez alguma tentativa para arranjar emprego	Sim <input type="checkbox"/>	Não <input type="checkbox"/>	
24. Já recebeu algum apoio para trabalhar?	Sim <input type="checkbox"/>	Não <input type="checkbox"/>	Qual? _____

#### D. Serviços pretendidos

25. Que tipo de serviços de apoio à reintegração recebeu ou pretende receber do Programa Geral de Desmobilização e Reintegração (PGDR)?	Agricultura <input type="checkbox"/>	Formação e apoio a Act. de Rendimento Não Agrícola <input type="checkbox"/>	Integração em Trabalhos Comunitários <input type="checkbox"/>
26. O que pretende fazer após receber esses serviços?	Agricultura <input type="checkbox"/>	Desenvolver uma Act. de Rendimento Não Agrícola <input type="checkbox"/>	Integração em Trabalhos Comunitários <input type="checkbox"/>
27. Acha que, caso recebesse esse apoio, tal ajudaria à sua reintegração?	Muito <input type="checkbox"/>	Pouco <input type="checkbox"/>	Nada <input type="checkbox"/>

Caso não tenha recebido qualquer apoio de kit agrícola, conclua aqui o questionário.

28. Como é que usou esse kit??	Para trabalhar por conta própria <input type="checkbox"/>	Cedeu-o a familiares <input type="checkbox"/>	Vendeu-o <input type="checkbox"/>
29. Se o utilizou para trabalhar por conta própria, que resultados obteve?	Bons <input type="checkbox"/>	Razoáveis <input type="checkbox"/>	Maus <input type="checkbox"/>

**E. Observações:**

\_\_\_\_\_

## O Beneficiário

O Entrevistador,

Lançado na base de dados em: ____/____/____	Por:
---	------
